

Please see this weeks update.

For ease of reading all significant updates are highlighted in red.

Works have progressed this week with 140m lined in addition to 98m lined the previous week.

Progress Update:

- **The total sealed to date is 13,980m across both public and private sewer networks.**

Any tanker activity associated with the sewer lining works will conclude today. Glenn returns from annual leave on Monday, so I will provide a further update early next week once I have had the opportunity to speak with him and the wider team.


Please note that a sealing team will remain in the area to carry out follow-up works, sealing the manholes along sections of the network where the sewer lining has already been completed. These works are expected to continue for approximately three weeks.

As always, please see borehole data from Chilgrove below which shows the ground water levels for your reference.

Borehole	Latest level	Date
Chilgrove	42.55	3 Jul 2026

Date ^		Rise (or fall) in the last 24 hours (m)
29 Jun 2026, 00:00	↓	-0.089
30 Jun 2026, 00:00	↓	-0.139
1 Jul 2026, 00:00	↓	-0.109
2 Jul 2026, 00:00	↓	-0.093
3 Jul 2026, 00:00	↓	-0.111

Data Studio

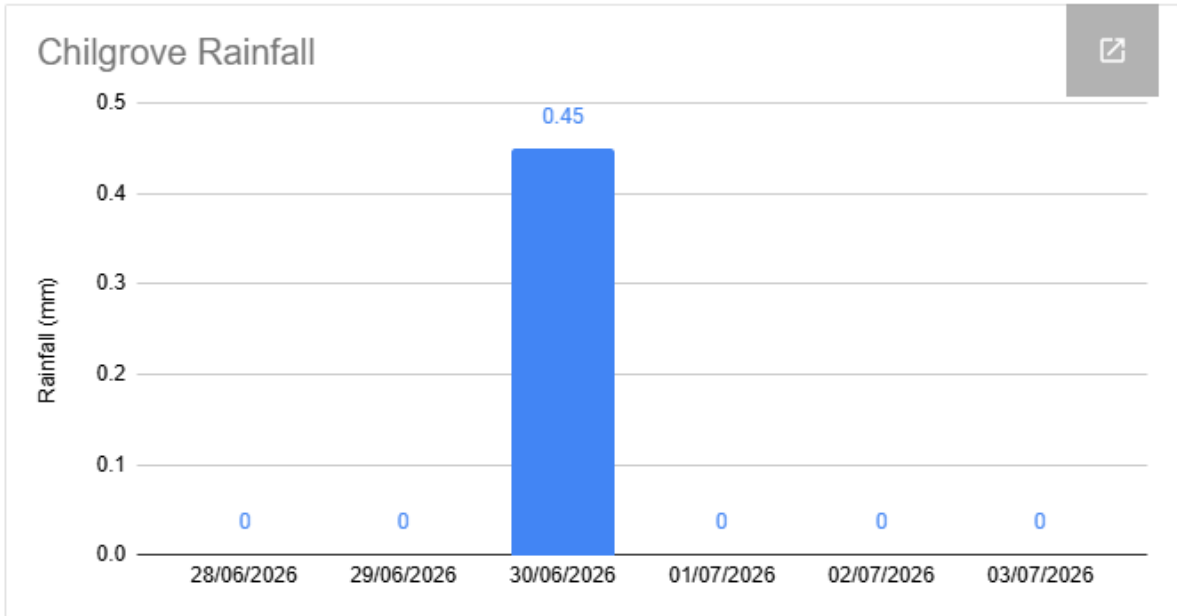

The ground water continues to fall and we will monitor this to find more localised issues created by this years ground water season.
