

Please see this weeks update.

For ease of reading all significant updates are highlighted in red.

Works have been progressing this week with 150m of public and private sewer lined.

Progress Update:

- **The total sealed to date is 13,742m across both public and private sewer networks.**

We continue to have 2 manhole sealing teams in the Lavant valley between East Dean and West Dean.

Whilst also having our contractor MTS checking the condition of the sewer sealing in the same area.

As of yet we have not found any issues with the sewer sealing material installed. We have however located some manholes that are still allowing ground water to infiltrate into the wastewater system, these will be dealt with accordingly as the manhole teams are on site.

Aside from the above, it's business as usual as we continue progressing with the task at hand.


I've also included the **borehole data from Chilgrove** below which shows the ground water levels for your reference.

Borehole	Latest level	Date
Chilgrove	44.172	19 Jun 2026

Date ^		Rise (or fall) in the last 24 hours (m)
15 Jun 2026, 00:00	↓	-0.126
16 Jun 2026, 00:00	↓	-0.088
17 Jun 2026, 00:00	↓	-0.119
18 Jun 2026, 00:00	↓	-0.127
19 Jun 2026, 00:00	↓	-0.12

Data Studio

Chilgrove Rainfall

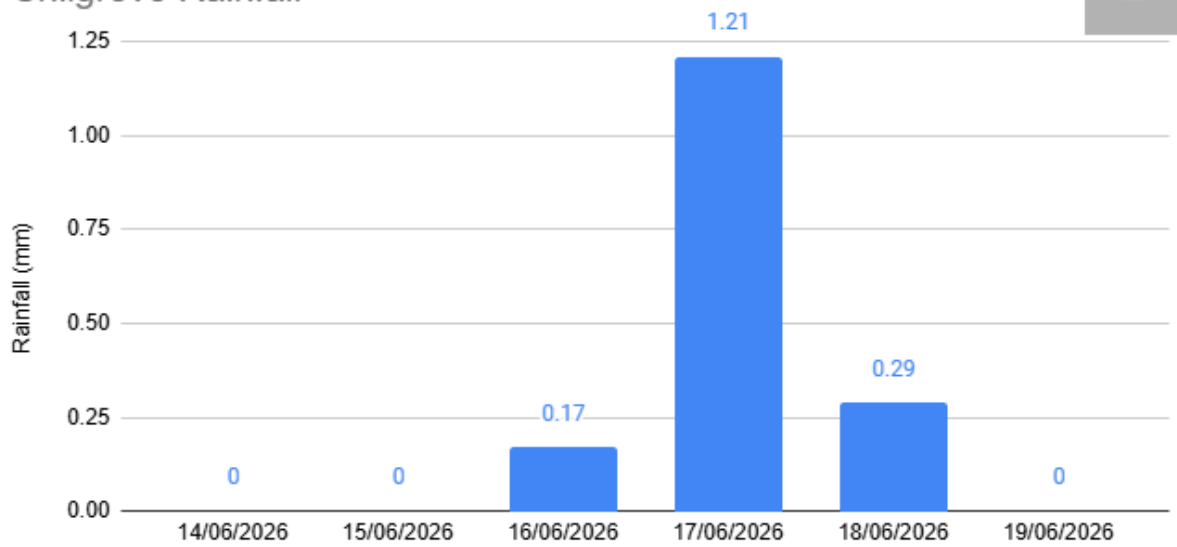

The ground water continues to fall and we will monitor this to find more localised issues created by this years ground water season.
