

Please see this weeks update.

For ease of reading all significant updates are highlighted in red.

Works have been progressing this week with 145m of public and private sewer lined.

Progress Update:

- **The total sealed to date is 13,387m across both public and private sewer networks.**

We also have in the Lavant valley between East Dean and West Dean 2 x manhole sealing teams.

We also have our contractor MTS checking the condition of the sewer sealing from East Dean down to West Dean as yet we have found no issues with the sewer sealing material installed and we have located some manholes that are still allowing ground water to infiltrate into the waste water system which will be dealt with now as the manhole team are onsite.


Aside from the above, it's business as usual as we continue progressing with the task at hand.

I've also included the **borehole data from Chilgrove** below which shows the ground water levels for your reference.

Borehole	Latest level	Date
East Dean Butchers Lane	70.937	May 29, 2026

Date	Rise (or fall) in the last 24 hours (m)
May 25, 2026, 12:00 AM	-0.088
May 26, 2026, 12:00 AM	-0.083
May 27, 2026, 12:00 AM	-0.087
May 28, 2026, 12:00 AM	-0.085
May 29, 2026, 12:00 AM	-0.085

Chilgrove Rainfall

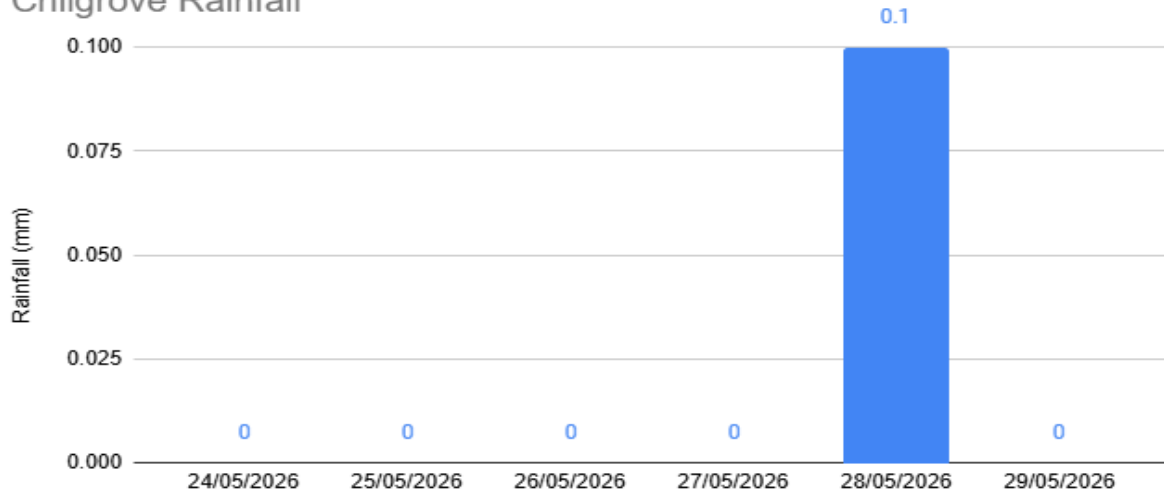

The ground water continues to fall and we will monitor this to find more localised issues created by this years ground water season.

“ When there is teamwork and collaboration wonderful things can be achieved “
