

Please see this weeks update.

For ease of reading all significant updates are highlighted in red.

Works have been progressing this week with 160m of public and private sewer lined.

The surveying of all the sealing works undertaken to date have continued and will be continuing for the foreseeable future.

At this stage, we have **not identified any failed sewer sealing works.**

Once our surveys are complete, we will discuss a remedial plan with our manhole sealing team to reduce infiltration that is entering the network via the private inspection chambers we identify.

Progress Update:

- **The total sealed to date is 13,062m across both public and private sewer networks.**

East Dean:

Thank you to everyone who attended the meeting at the village hall on Tuesday evening. I found it to be a constructive and helpful discussion.

For any questions I wasn't able to answer on the night, Glenn has kindly followed up, and these responses have been shared with the Parish Council Chair.

As some of you may have noticed, this was my first public speaking event, so I really appreciated your understanding, respect, and your thoughtful and direct questions.


And then finally, aside from the above, it's business as usual as we continue progressing with the task at hand.

I've also included the **borehole data from Chilgrove** below which shows the ground water levels for your reference.

Borehole	Latest level	Date
Chilgrove	51.329	8 May 2026

Date ▲		Rise (or fall) in the last 24 hours (m)
4 May 2026, 00:00	↓	-0.263
5 May 2026, 00:00	↓	-0.224
6 May 2026, 00:00	↓	-0.265
7 May 2026, 00:00	↓	-0.239
8 May 2026, 00:00	↓	-0.227

Data Studio

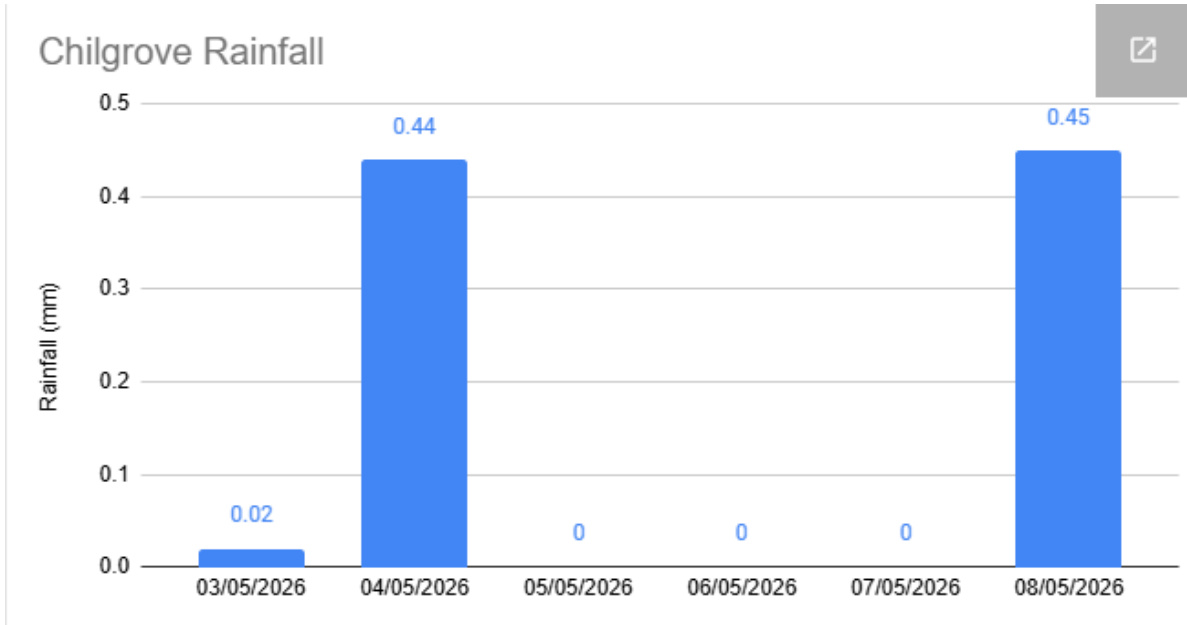

The ground water continues to fall and we will monitor this to find more localised issues created by this years ground water season.

We will continue to investigate and fix as we find the issues as quickly as possible to get the tankers away from the catchment.
