

As my last update was on Tuesday this one will be largely unchanged.

We are going to survey all the sealing that has been undertaken and following this we will discuss a remedial plan with our manhole sealing team to reduce infiltration that is entering the network via the private inspection chambers we identified.

At this stage, we have **not** identified any failed sewer sealing works.

**Progress Update:**

- **The crews sealed approximately 78m of public and private sewer in Singleton and East Dean last week.**
- **This brings the total sealed to date to around 12,291m across both public and private sewer networks.**

Aside from the above, it's business as usual as we continue progressing with the task at hand.


I've also included the **borehole data from Chilgrove** below which shows the ground water levels for your reference.

Borehole	Latest level	Date
Chilgrove	59.768	9 Apr 2026

Date	Rise (or fall) in the last 24 hours (m)
5 Apr 2026, 00:00	-0.347
6 Apr 2026, 00:00	-0.384
7 Apr 2026, 00:00	-0.328
8 Apr 2026, 00:00	-0.365
9 Apr 2026, 00:00	-0.336

Chilgrove Rainfall

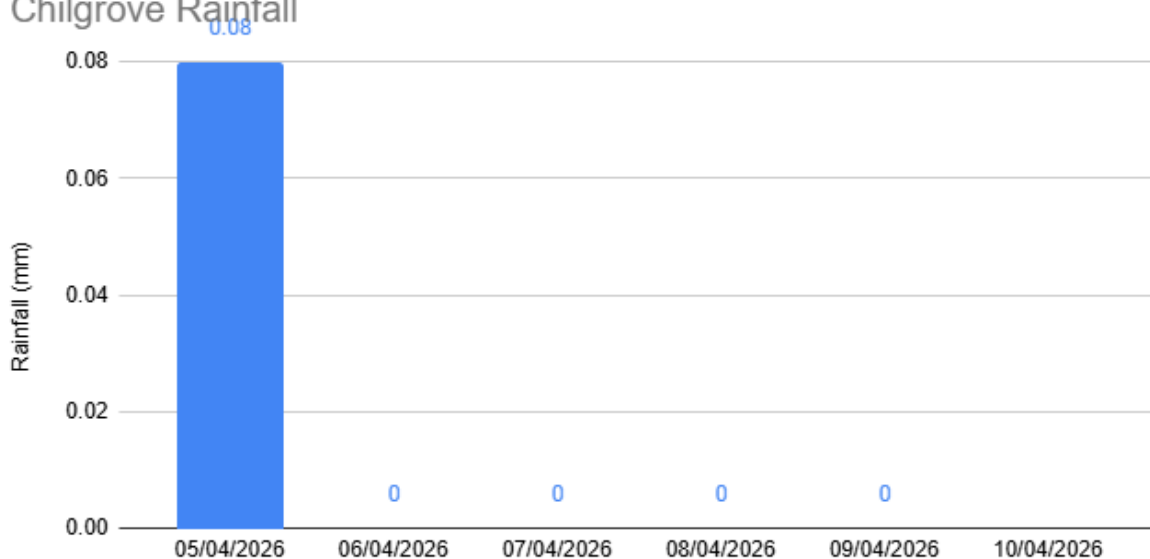

The ground water continues to fall and we will monitor this to find more localised issues created by this years ground water season.

We will continue to investigate and fix as we find the issues as quickly as possible to get the tankers away from the catchment.
