

Please see this weeks update.

For ease of reading all significant updates are highlighted in red.

Works have continued this week to survey all the sealing works undertaken to date and these will be continuing for the foreseeable future.

At this stage, we have **not identified any failed sewer sealing works.**

Once our surveys are complete, we will discuss a remedial plan with our manhole sealing team to reduce infiltration that is entering the network via the private inspection chambers we identify.

Progress Update:

- **The total sealed to date is 12,531m across both public and private sewer networks.**

Aside from the above, it's business as usual as we continue progressing with the task at hand.


I've also included the **borehole data from Chilgrove** below which shows the ground water levels for your reference.

Borehole	Latest level	Date
Chilgrove	54.957	24 Apr 2026

Date ▲		Rise (or fall) in the last 24 hours (m)
20 Apr 2026, 00:00	↓	-0.286
21 Apr 2026, 00:00	↓	-0.315
22 Apr 2026, 00:00	↓	-0.273
23 Apr 2026, 00:00	↓	-0.338
24 Apr 2026, 00:00	↓	-0.272

Data Studio

Chilgrove Rainfall

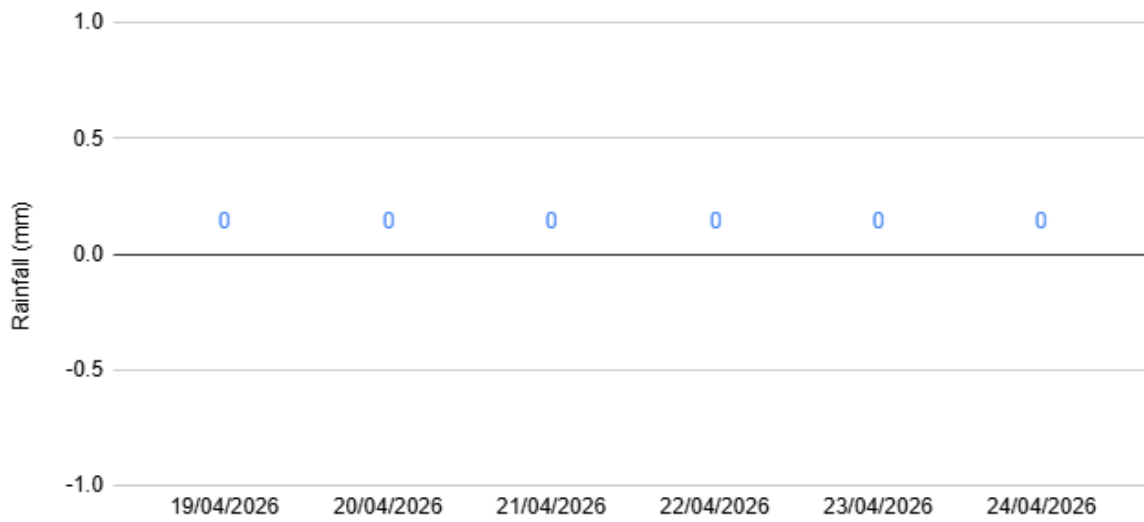

The ground water continues to fall and we will monitor this to find more localised issues created by this years ground water season.

We will continue to investigate and fix as we find the issues as quickly as possible to get the tankers away from the catchment.
